### **Hawkesdale Wind Farm**


## Weekly Construction Report May 1, 2023


# GPG Naturgy Group



A major milestone achieved this week with the pouring of the first foundation.

The short week did not slow this down, everyone was well prepared and the construction is steadily moving along. Traffic management was in place to ensure that all the extra movements across the wind farm were done safely.

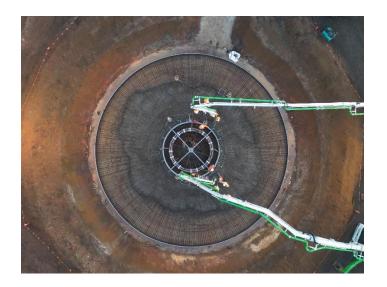

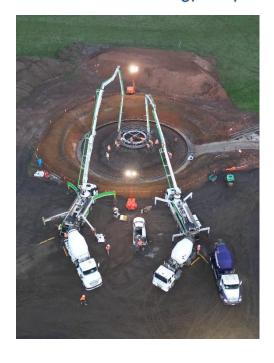

#### Access tracks and turbine locations:

The first foundation pour signifies a major milestone in the construction of any wind farm. The amount of concrete in a foundation varies depending on the location and the conditions of the soil. The first foundation had approximately 475 m<sup>3</sup> of concrete, all of this is from the on-site batch plant. concrete trucks take the concrete from the batch plant to the concrete pumps at the foundation.

### **Connections:**

The trencher has arrived on site and should start with the internal trenches next week.

Construction continues at the Tarrone terminal station to prepare for the delivery of the large transformer.

