


Hawkesdale Wind Farm

Weekly Construction Report

July 17, 2023

General:

Work is progressing steadily on site with the better weather. Work has commenced on the intersection upgrades required for the over dimensional loads that transport the turbine components to site. Vestas has commenced delivering containers and will start establishing their site compound area in the next 2 weeks.

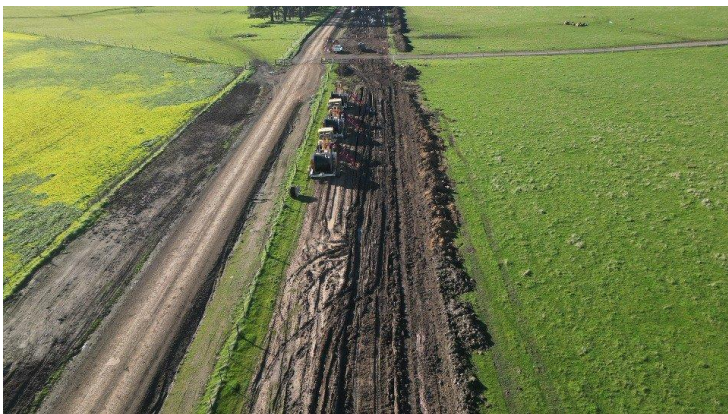

Access tracks and turbine locations:

18 foundations have been back-filled.

The northern foundations are undergoing final trim and topsoil in readiness for handover to the wind turbine installation team.

Vestas have started to bring equipment to site in readiness for wind turbine installation.



Connections:

Three underground cable collector circuits have been installed on the north side of the wind farm with a final run to the site substation planned in the upcoming weeks. The electrical contractor will move their equipment to the south side of the wind farm this week to begin the installation of cable along that section. Excavations has started on the internal substation and operations building site.

Hawkesdale Asset Trust

Phone: 0428 867 646 (Debra Dumesny – Community and Stakeholder Engagement)

Email: hawkesdalewindfarm@globalpower-generation.com.au or debra.dumesny@globalpower-generation.com.au

Website: www.hawkesdalewindfarm.com.au

Mail: Hawkesdale Asset Trust, Suite A, Level 3, 73 Northbourne Avenue, Canberra ACT 2601
